



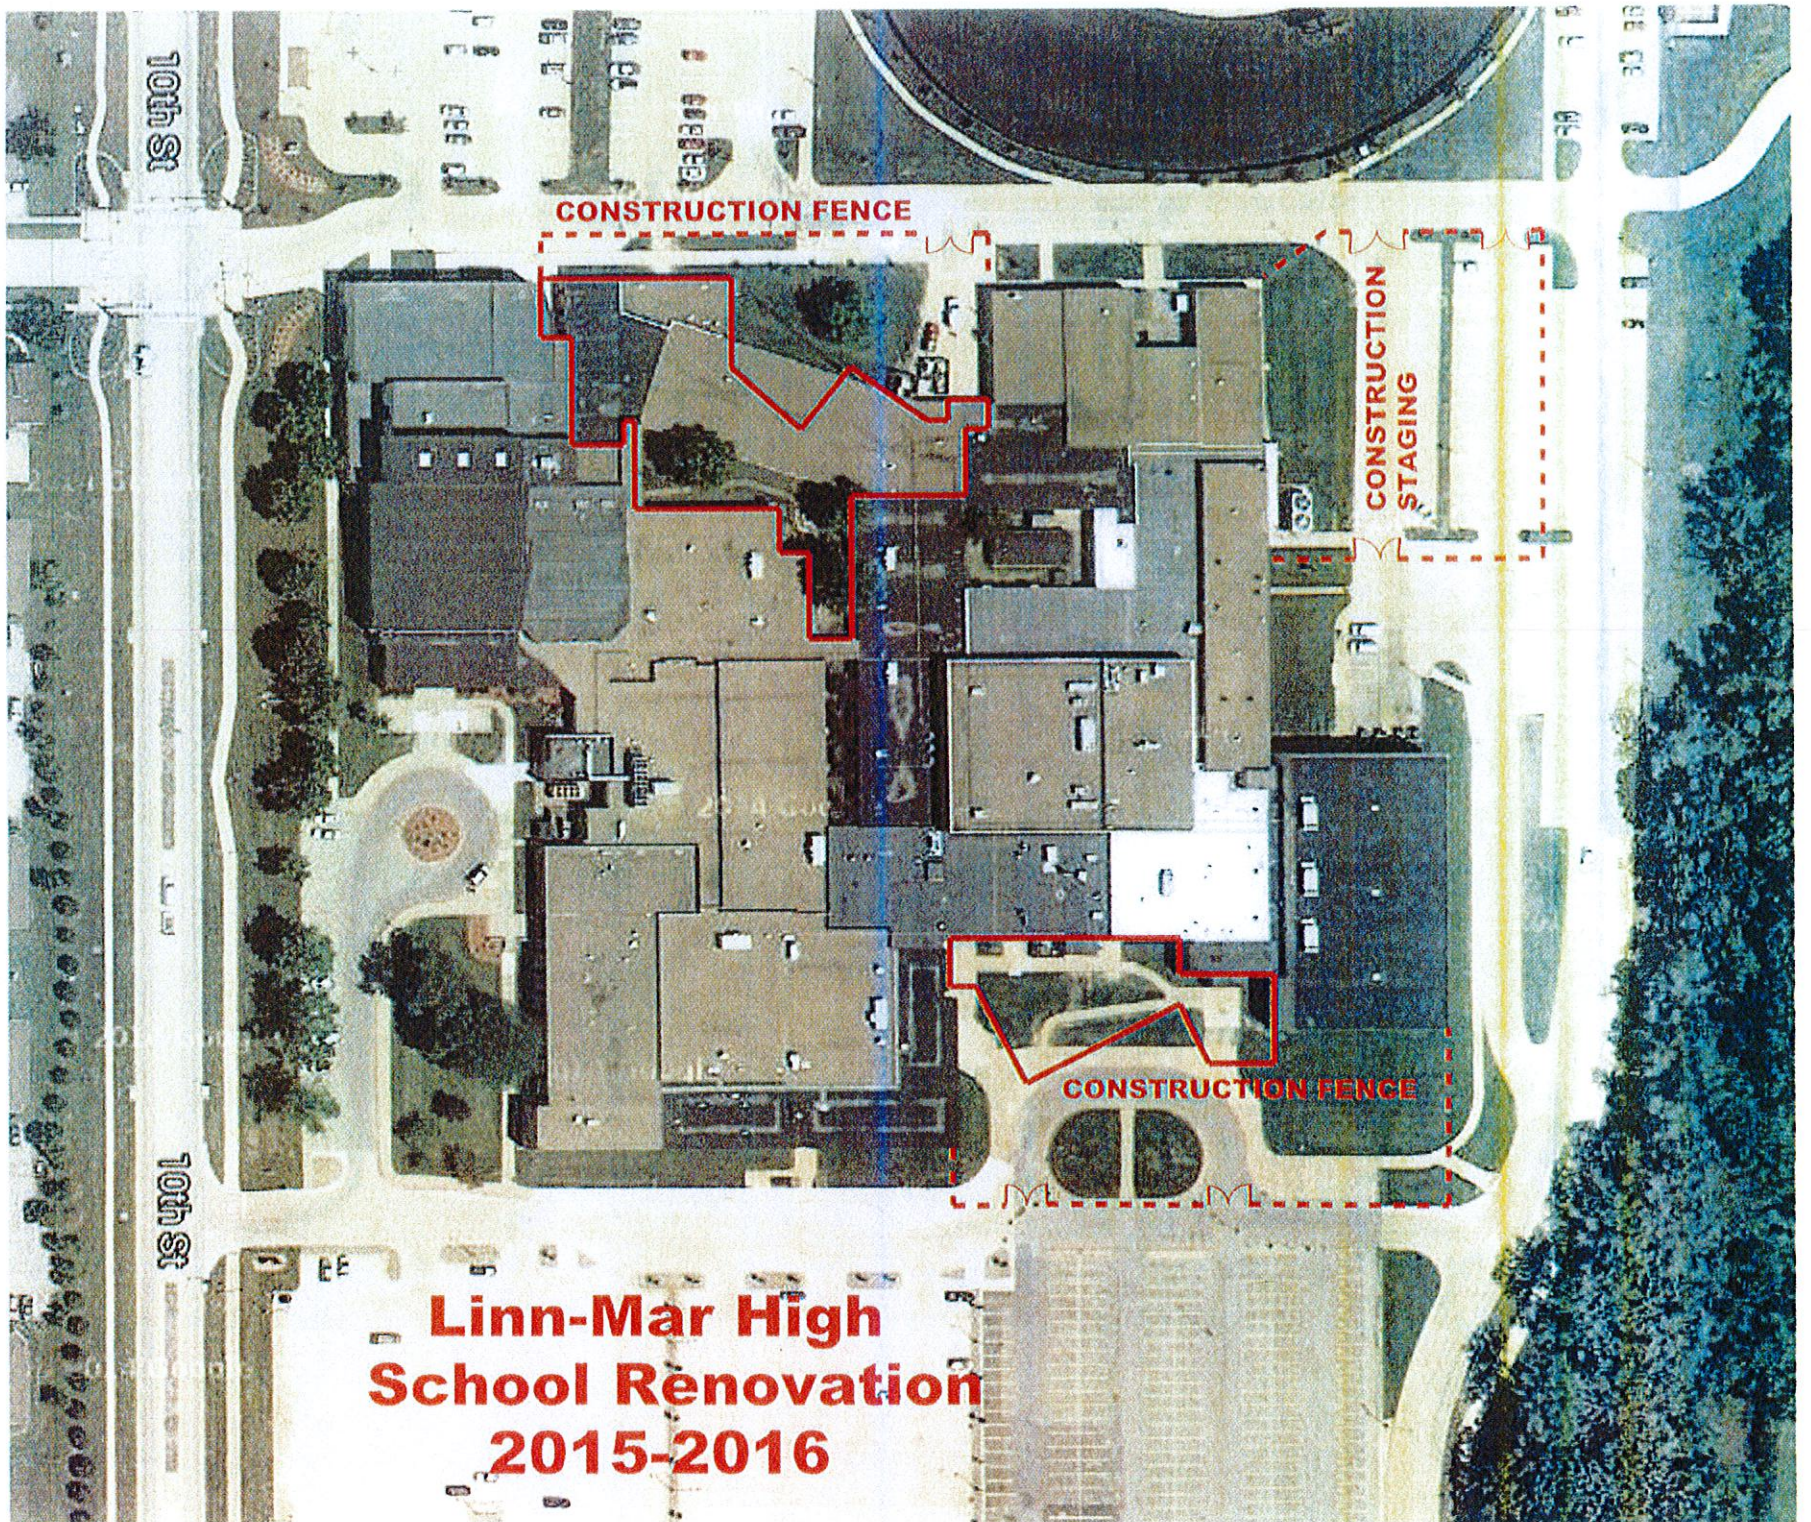

**Linn-Mar High
School Renovation
2015-2016**

Linn-Mar High School Construction Egress

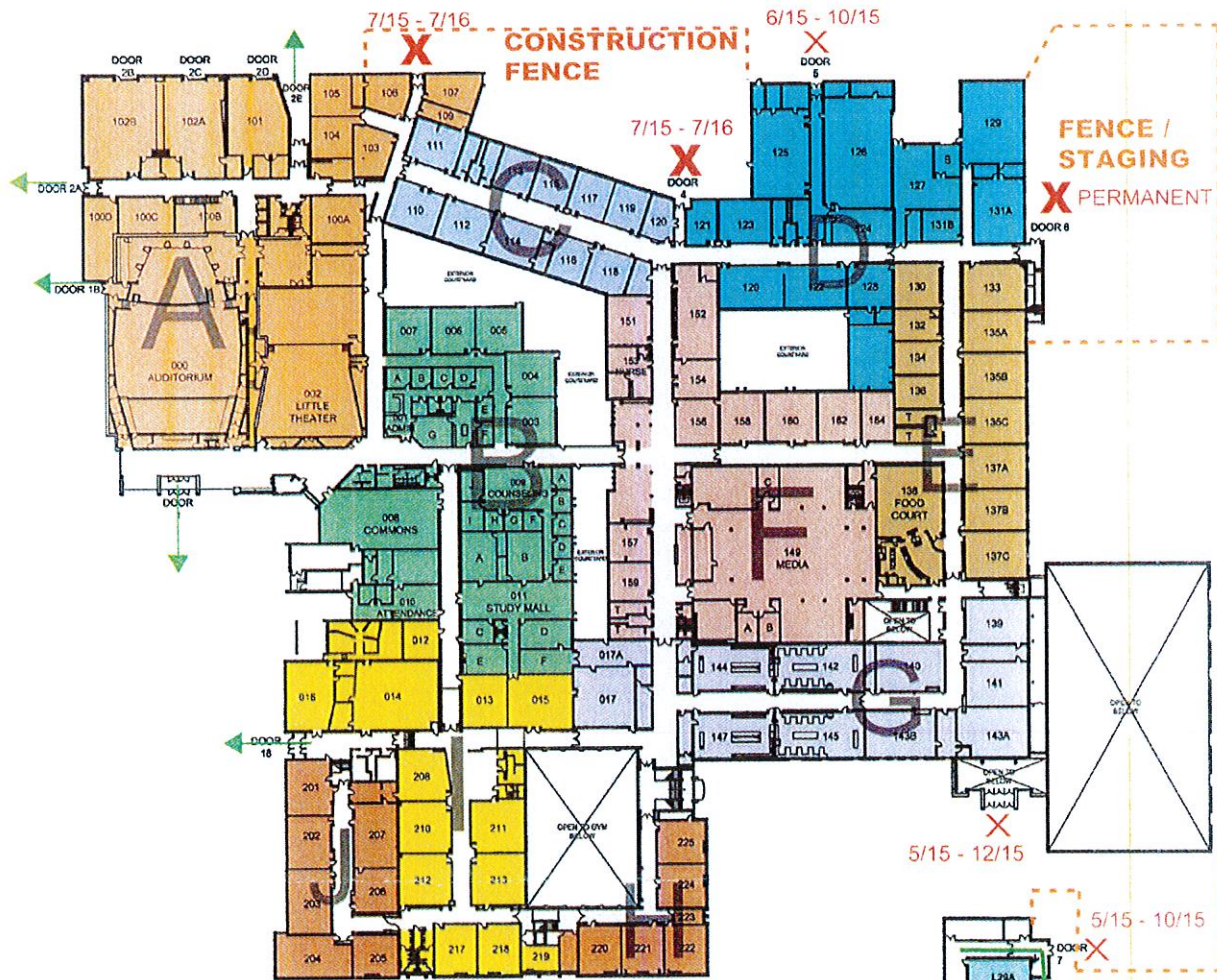

MAIN LEVEL


LEGEND

Construction Egress Summer to Fall

✕ TEMPORARY CLOSED EGRESS

➔ PERMANENT EGRESS

✕ CLOSED EGRESS
DURATION OF PROJECT

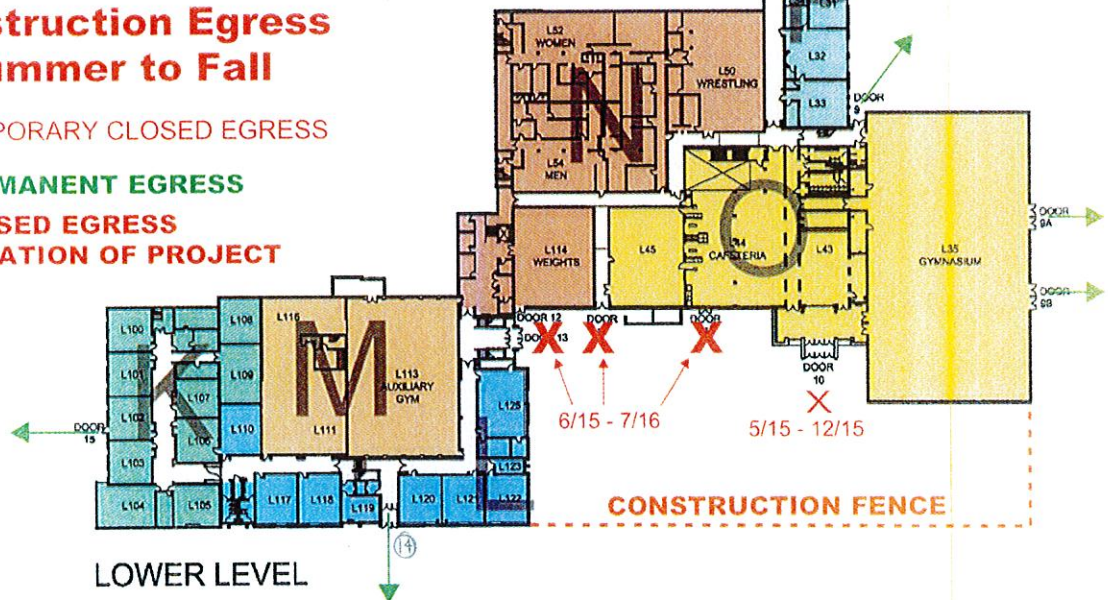


LOWER LEVEL




Linn -Mar High HS Additions & Renovations Phasing Diagram

DESCRIPTION	START	END
A Area E - East Stair Tower Demolition	May 1 2015	August 2015
B Area H - Communications Tower Relocation	March 16 2015	March 27 2015
C1 Area F - Art/Industrial Technology Renovation	June 2015	October 2015
C2 Area F - Family/Community Services Renovation	June 2015	December 2015
D Area B - Cafeteria Renovation	June 2015	August 2015
E1 Area C - Ground Level Classroom Renovations	June 2015	December 2015
E2 Area C - First Level Classroom Renovations	June 2015	December 2016
F1 Area F - Courtyard Greenhouse/Shed Demolition	June 2015	October 2015
F2 Area F - Classroom Improvements	June 2015	December 2015
G Area D - Media Center	June 2015	August 2016
H Area H - 1959/1973 Building Demolition	May 2 2015	August 2015
J Area H - North Building Addition	July 2 2015	July 2016
K Area E/H - FCS Program Relocation to New Space	After New Area Complete	August 2016
L Area M - Lecture Hall Renovation	After New Area Complete	August 2016
M1 Area E - Wrestling Room Construction	After New Area Complete	October 2016
M2 Area E - Fitness Area Renovation	After New Area Complete	October 2016
M3 Area E Classroom Conversion	After New Area Complete	August 2016
O Area B - South Entry Vestibule Demolition	May 1 2015	June 1 2015
P1 Area B/Area E - South Electrical Re Location	June 2015	August 2016
P2 Area B - South Mechanical Re Location	TBD	TBD
Q1 Area B - South Entry Addition	June 2015	December 2015
Q2 Area B - South Building Addition	June 2015	July 1 2016
R Areas B - Athletic Office Re-Location	Completion of South Add.	August 2016
B Entire Facility - Corridor/Restroom/Misc. Renovations		December 2016

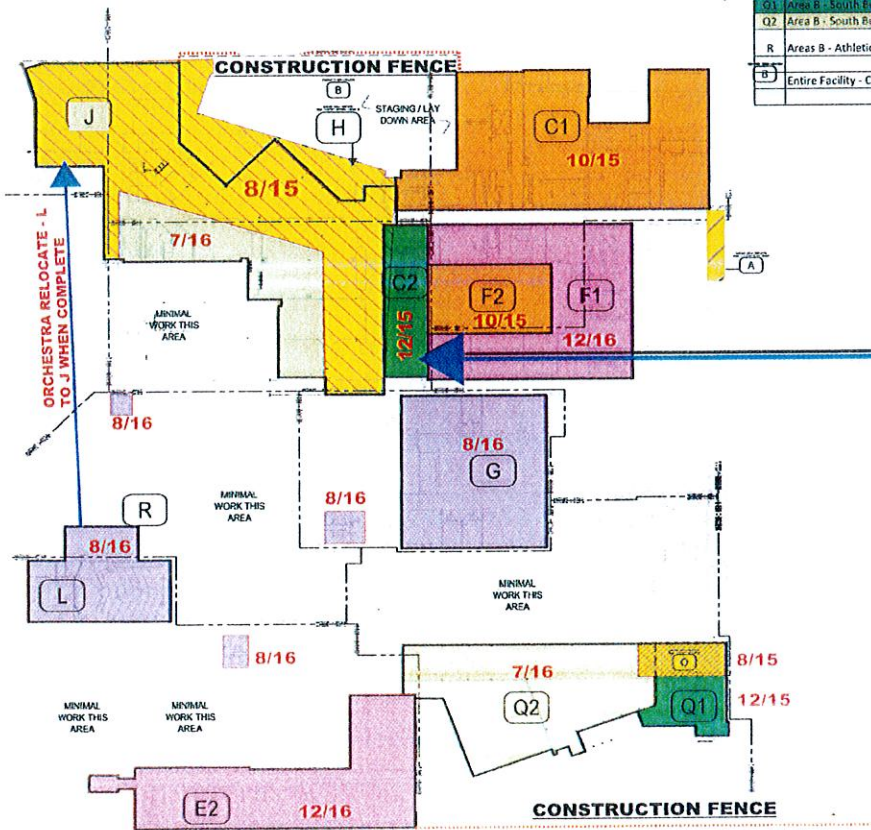

First Floor

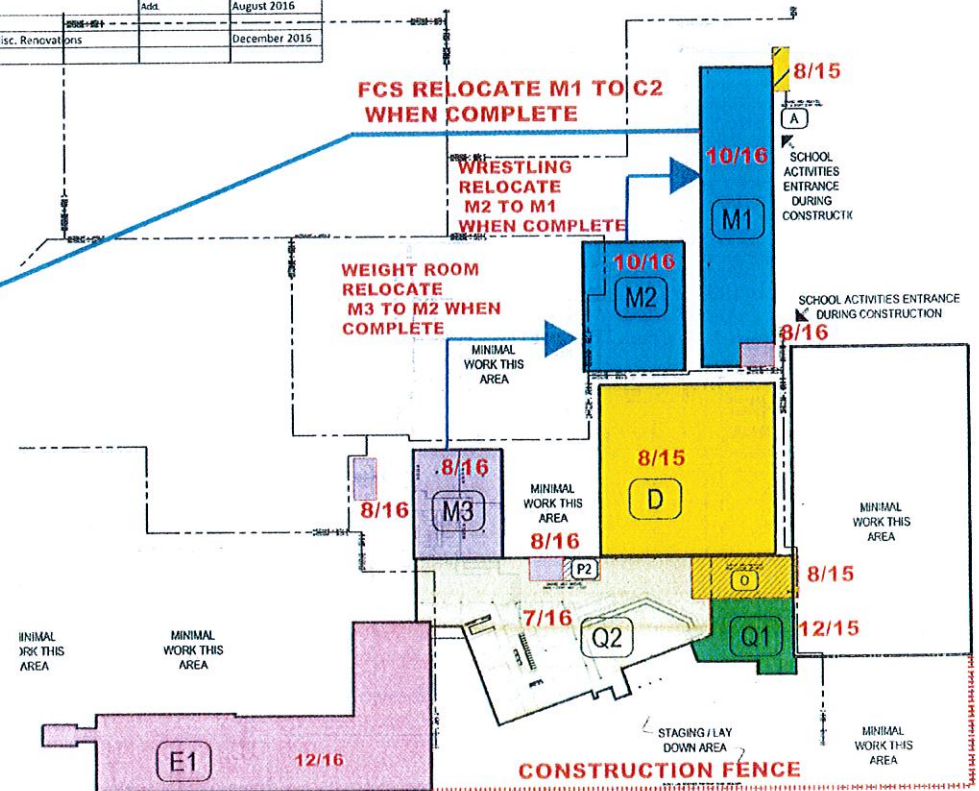

Ground Floor

High School Reno Update

4/20/15

Important Dates

LRC

- Moving Home School - 4/20 – 5/1
- Move 3rd Floor Staff – 5/4 – 5/22
- Move HS Teachers – 5/25 – 6/2
 - o Finals week and end of school

High School Project

- Larson Construction on Site – 4/20
 - o Fencing, Trailer
- Demo of Door 10 – 5/1 *
- Demo of East Stairwell – 5/4 *

2015 Phasing of Project

- DEM/Art Reno – 5/2 – 10/19
- Cafeteria Reno – 5/3 – 8/15
- North Hall Demo – 5/3 – 8/15
- South Entrance Excavation – 5/3 – 8/15
- South Entrance Mechanical/Electrical/Water – 5/3 – 8/15

Other HS Projects (Rick)

- Bleacher Replacement – 5/8 – 7/24
- Gym Floor Painting – Determined by bleacher project
- Stage Floor
- Tower Move – April – June
- High School Roof Replacement – 6/8 – 8/7
